

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	August 2023							Sept
								25	30	4	9	14	19	24	29
1		Avenue M to Avenue N	36 days	Tue 8/1/23	Tue 9/19/23										
2		Demo Existing Roadway	2 days	Tue 8/1/23	Wed 8/2/23										
3		Sanitary Sewer and Manholes 300' short of N	3 days	Thu 8/3/23	Mon 8/7/23	2									
4		8' x 3' RCB 300' short of N	8 days	Tue 8/8/23	Thu 8/17/23	3									
5		Inlets in Avenue M	4 days	Fri 8/18/23	Wed 8/23/23	4									
6		Base Stabilization	2 days	Mon 8/21/23	Tue 8/22/23	5									
7		Paving Setup	3 days	Wed 8/23/23	Fri 8/25/23	6									
8		Pour Concrete	1 day	Mon 8/28/23	Mon 8/28/23	7									
9		Sidewalk and Parking	6 days	Tue 8/29/23	Tue 9/5/23	8									
10		Brick Pavers	2 days	Wed 9/6/23	Thu 9/7/23	9									
11		Remainder sanitary	4 days	Mon 8/21/23	Thu 8/24/23										
12		Remainder RCB	8 days	Thu 8/24/23	Mon 9/4/23	11									
13		Remainder paving setup	4 days	Tue 9/5/23	Fri 9/8/23	12									
14		Remainder pour	1 day	Mon 9/11/23	Mon 9/11/23	13									
15		Remainder Sidewalk Driveway	6 days	Tue 9/12/23	Tue 9/19/23	14									
16		Avenue N to Avenue O	41 days	Wed 9/6/23	Wed 11/1/23										
17		Demo half Existing Roadway	2 days	Wed 9/6/23	Thu 9/7/23										

Project: 23rd Street Schedule 8.
Date: Fri 8/18/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	August 2023							Sept		
								25	30	4	9	14	19	24	29	3	
18		Sanitary Sewer and Manholes	7 days	Fri 9/8/23	Mon 9/18/23	17											
19		Reinforced Concrete Pipe	6 days	Mon 9/18/23	Mon 9/25/23	18											
20		Inlets in Avenue M	3 days	Mon 9/25/23	Wed 9/27/23	19											
21		Base Stabilization half width	2 days	Fri 9/29/23	Mon 10/2/23	20											
22		Paving Setup half width	5 days	Tue 10/3/23	Mon 10/9/23	21											
23		Pour Concrete half width	1 day	Tue 10/10/23	Tue 10/10/23	22											
24		Sidewalk and Parking	7 days	Wed 10/11/23	Thu 10/19/23	23											
25		Brick Pavers	2 days	Thu 10/19/23	Fri 10/20/23	24											
26		Demo other half	2 days	Thu 10/19/23	Fri 10/20/23	24											
27		Inlets	3 days	Mon 10/23/23	Wed 10/25/23	26											
28		Base stabilization	2 days	Wed 10/25/23	Thu 10/26/23	27											
29		paving setup	5 days	Wed 10/25/23	Tue 10/31/23	28											
30		pour concrete	1 day	Wed 11/1/23	Wed 11/1/23	29											
31		Avenue O to Avenue P	46 days	Thu 10/26/23	Thu 12/28/23												
32		Demo half Existing Roadway	2 days	Thu 10/26/23	Fri 10/27/23	27											
33		Sanitary Sewer and Manholes	6 days	Mon 10/30/23	Mon 11/6/23	32											

Project: 23rd Street Schedule 8.
Date: Fri 8/18/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	August 2023							Sept		
								25	30	4	9	14	19	24	29	3	
34		Reinforced Concrete Pipe	5 days	Tue 11/7/23	Mon 11/13/23	33											
35		Inlets in Avenue M	4 days	Tue 11/14/23	Fri 11/17/23	34											
36		Base Stabilization half	2 days	Mon 11/20/23	Tue 11/21/23	35											
37		Paving Setup half	5 days	Wed 11/22/23	Tue 11/28/23	36											
38		Pour Concrete half	1 day	Wed 11/29/23	Wed 11/29/23	37											
39		Sidewalk and Parking half	6 days	Thu 11/30/23	Thu 12/7/23	38											
40		Brick Pavers	2 days	Fri 12/8/23	Mon 12/11/23	39											
41		demo other half	2 days	Fri 12/8/23	Mon 12/11/23	39											
42		inlets	2 days	Tue 12/12/23	Wed 12/13/23	41											
43		base stabilization half	2 days	Tue 12/12/23	Wed 12/13/23	41											
44		setup half	4 days	Thu 12/14/23	Tue 12/19/23	43											
45		pour half	1 day	Wed 12/20/23	Wed 12/20/23	44											
46		sidewalk drives half	6 days	Thu 12/21/23	Thu 12/28/23	45											
47		Avenue P to Seawall	41 days	Thu 12/14/23	Thu 2/8/24												
48		Demo half Existing Roadway	2 days	Thu 12/14/23	Fri 12/15/23	42											
49		Sanitary Sewer and Manholes	6 days	Mon 12/18/23	Mon 12/25/23	48											
50		Reinforced Concrete Pipe	5 days	Tue 12/26/23	Mon 1/1/24	49											
51		Inlets in Avenue M	4 days	Tue 1/2/24	Fri 1/5/24	50											

Project: 23rd Street Schedule 8.
Date: Fri 8/18/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	August 2023							Sept		
								25	30	4	9	14	19	24	29	3	
52		Base Stabilization half	2 days	Mon 1/8/24	Tue 1/9/24	51											
53		Paving Setup half	5 days	Wed 1/10/24	Tue 1/16/24	52											
54		Pour Concrete half	1 day	Wed 1/17/24	Wed 1/17/24	53											
55		Sidewalk and Parking half	6 days	Thu 1/18/24	Thu 1/25/24	54											
56		Brick Pavers	2 days	Fri 1/26/24	Mon 1/29/24	55											
57		demo other half	2 days	Fri 1/26/24	Mon 1/29/24	55											
58		inlets	3 days	Mon 1/29/24	Wed 1/31/24	57											
59		base stabilization	2 days		Wed 1/31/24	58											
60		setup	4 days	Wed 1/31/24	Mon 2/5/24	59											
61		pour	1 day	Thu 2/1/24	Thu 2/1/24	60											
62		sidewalks	5 days	Fri 2/2/24	Thu 2/8/24	61											
63		Demobilization	21 days	Fri 2/9/24	Fri 3/8/24												
64		Punch List Items	15 days	Fri 2/9/24	Thu 2/29/24	62											
65		Site Cleanup	5 days	Fri 3/1/24	Thu 3/7/24	64											
66		Demobilization	1 day	Fri 3/8/24	Fri 3/8/24	65											




Project: 23rd Street Schedule 8.
Date: Fri 8/18/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

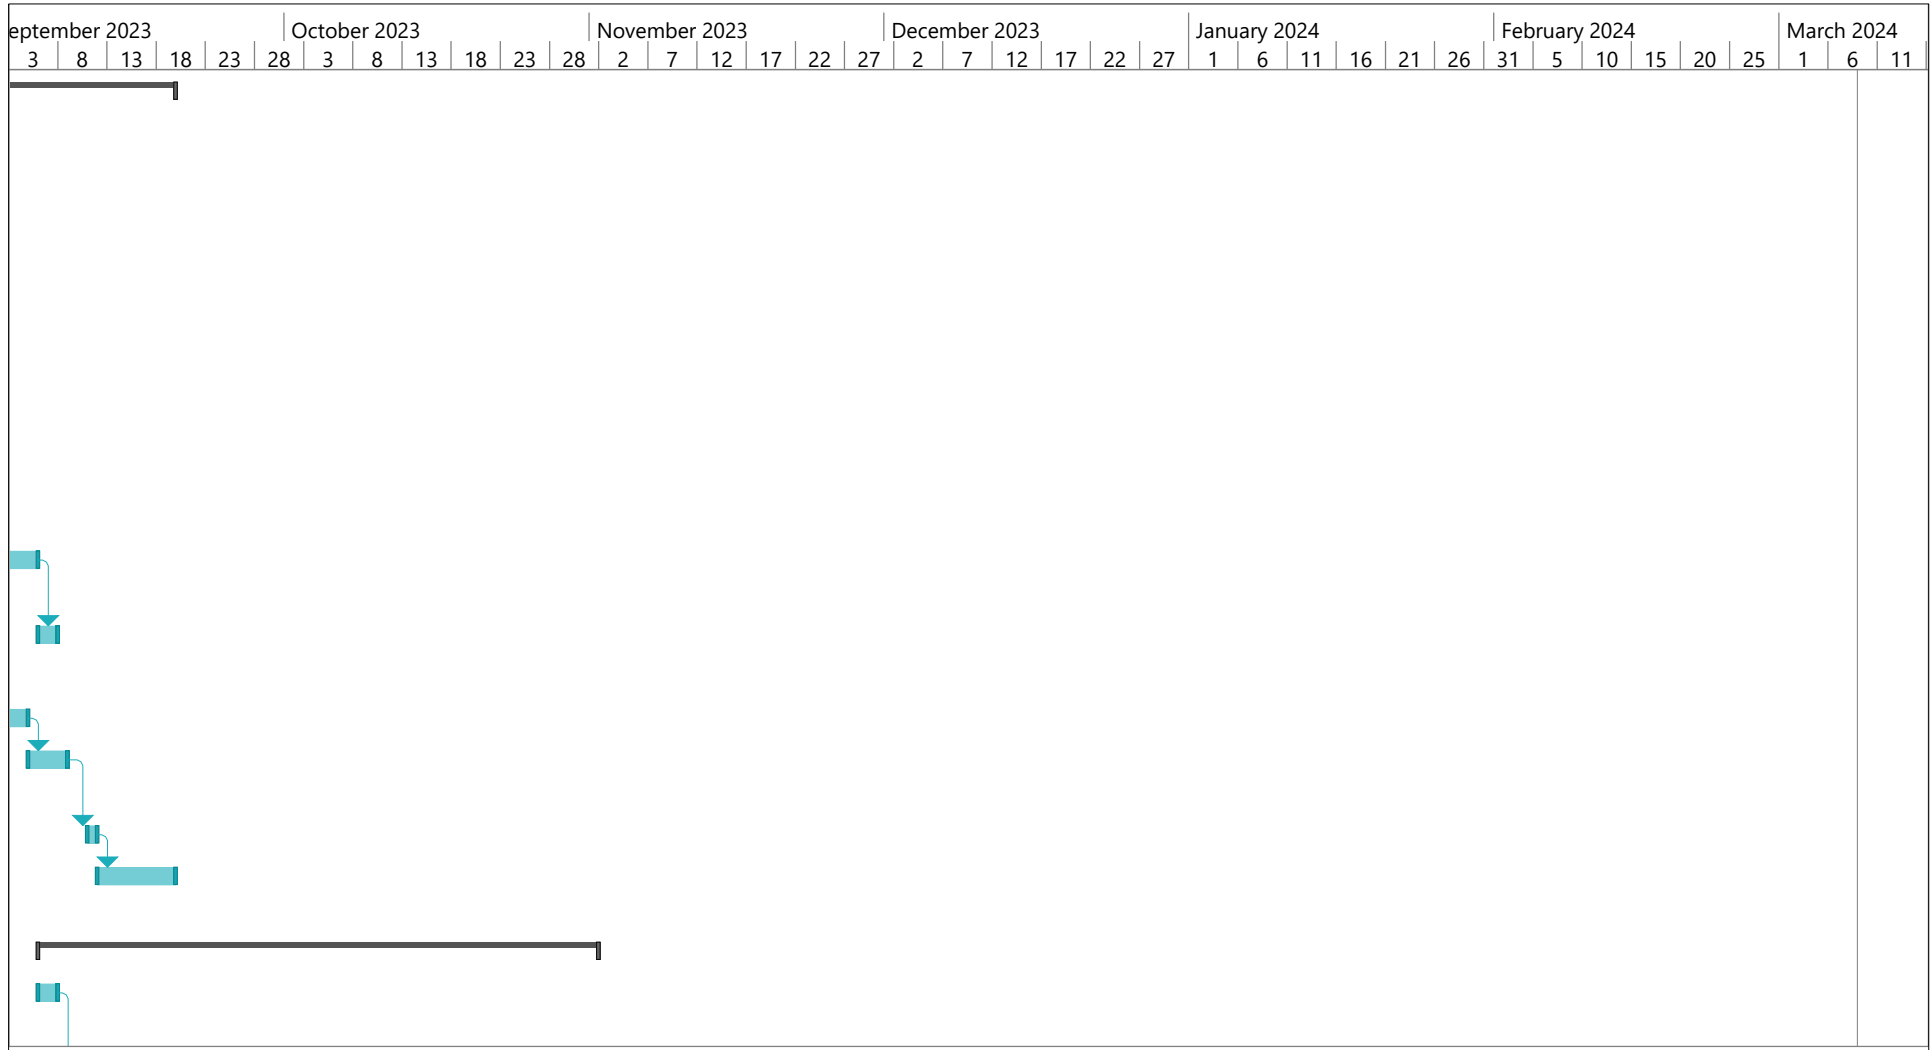


Project: 23rd Street Schedule 8.
Date: Fri 8/18/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

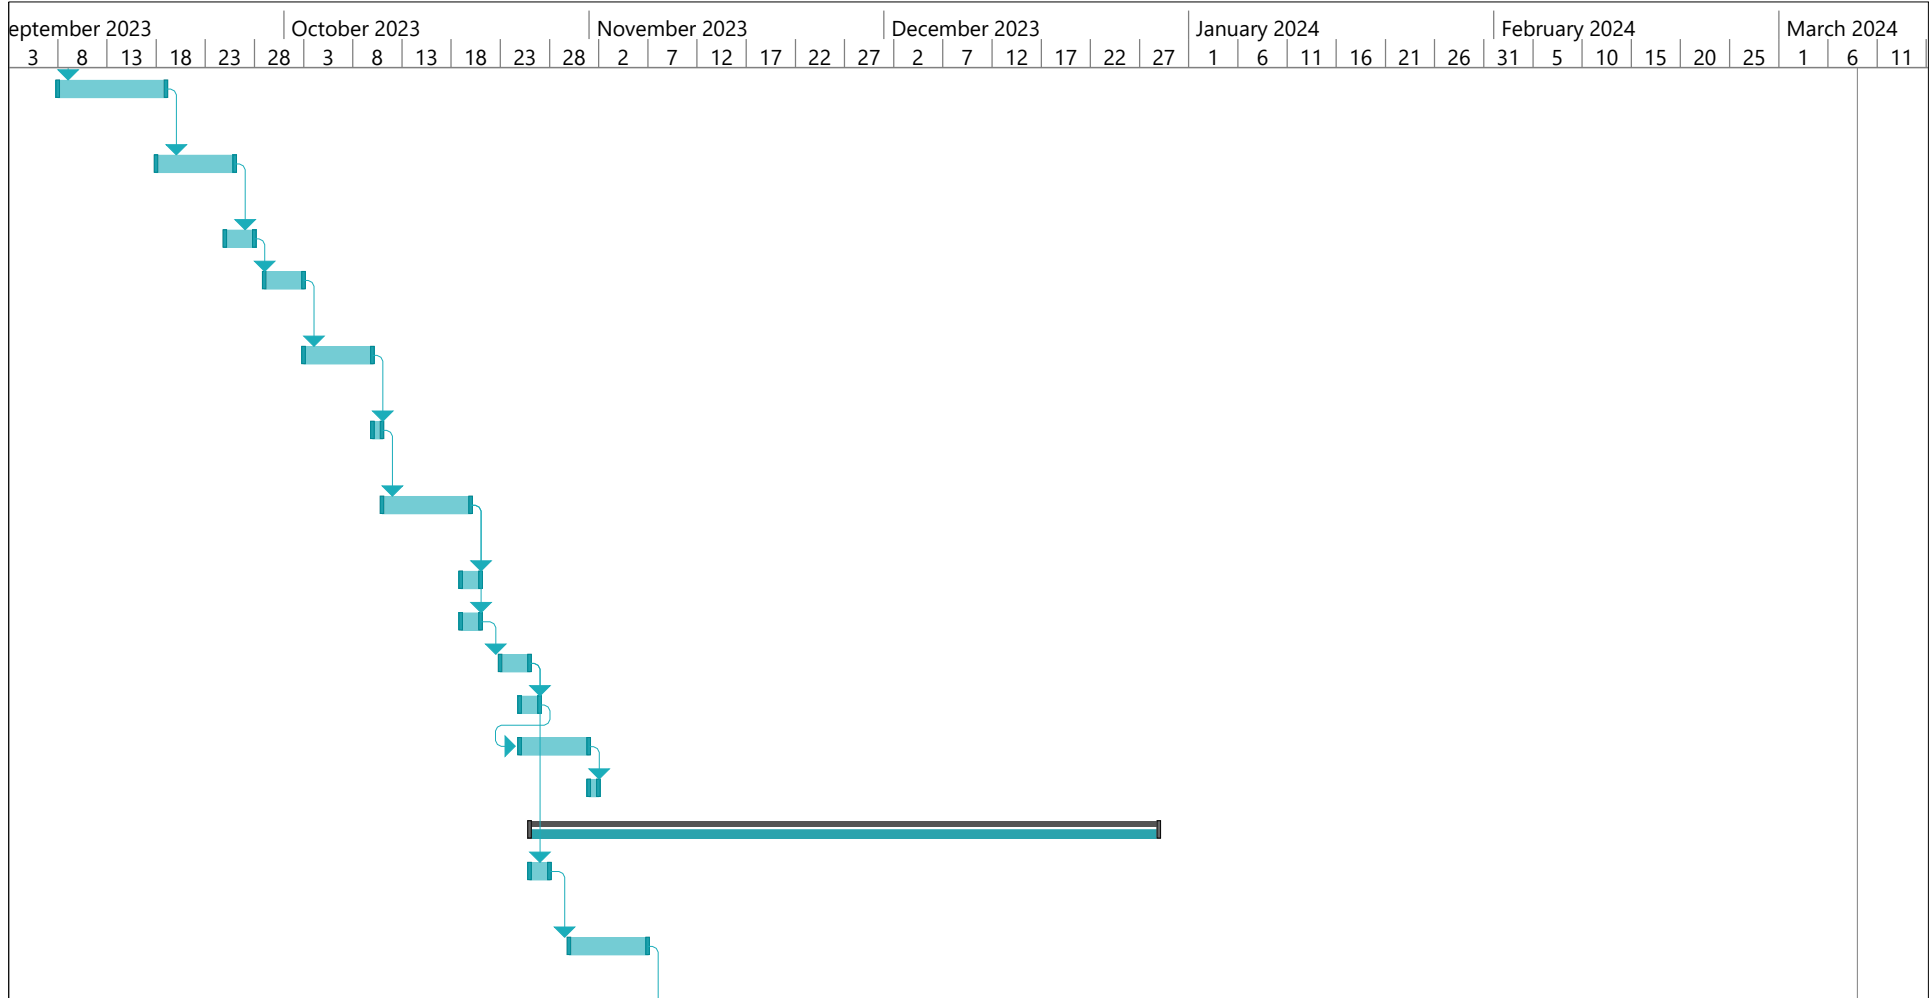


Project: 23rd Street Schedule 8.
Date: Fri 8/18/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

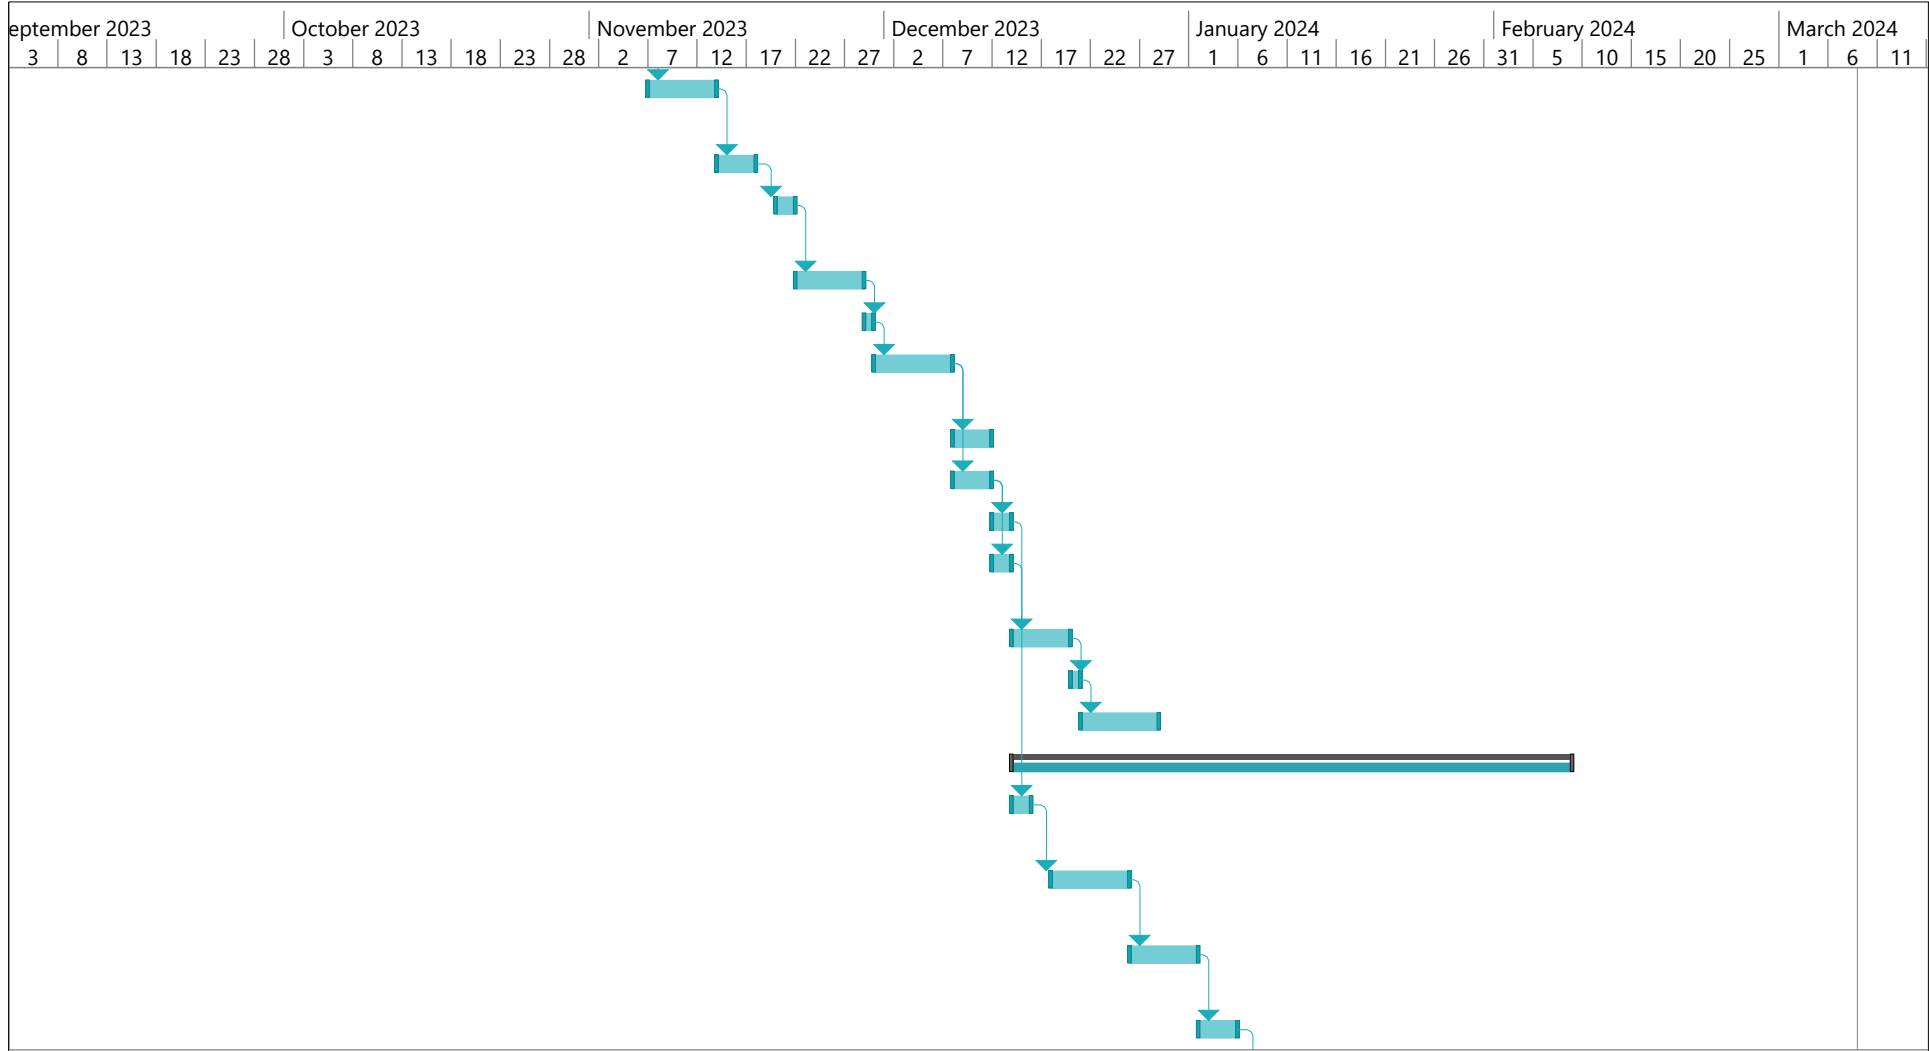

Project: 23rd Street Schedule 8. Date: Fri 8/18/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

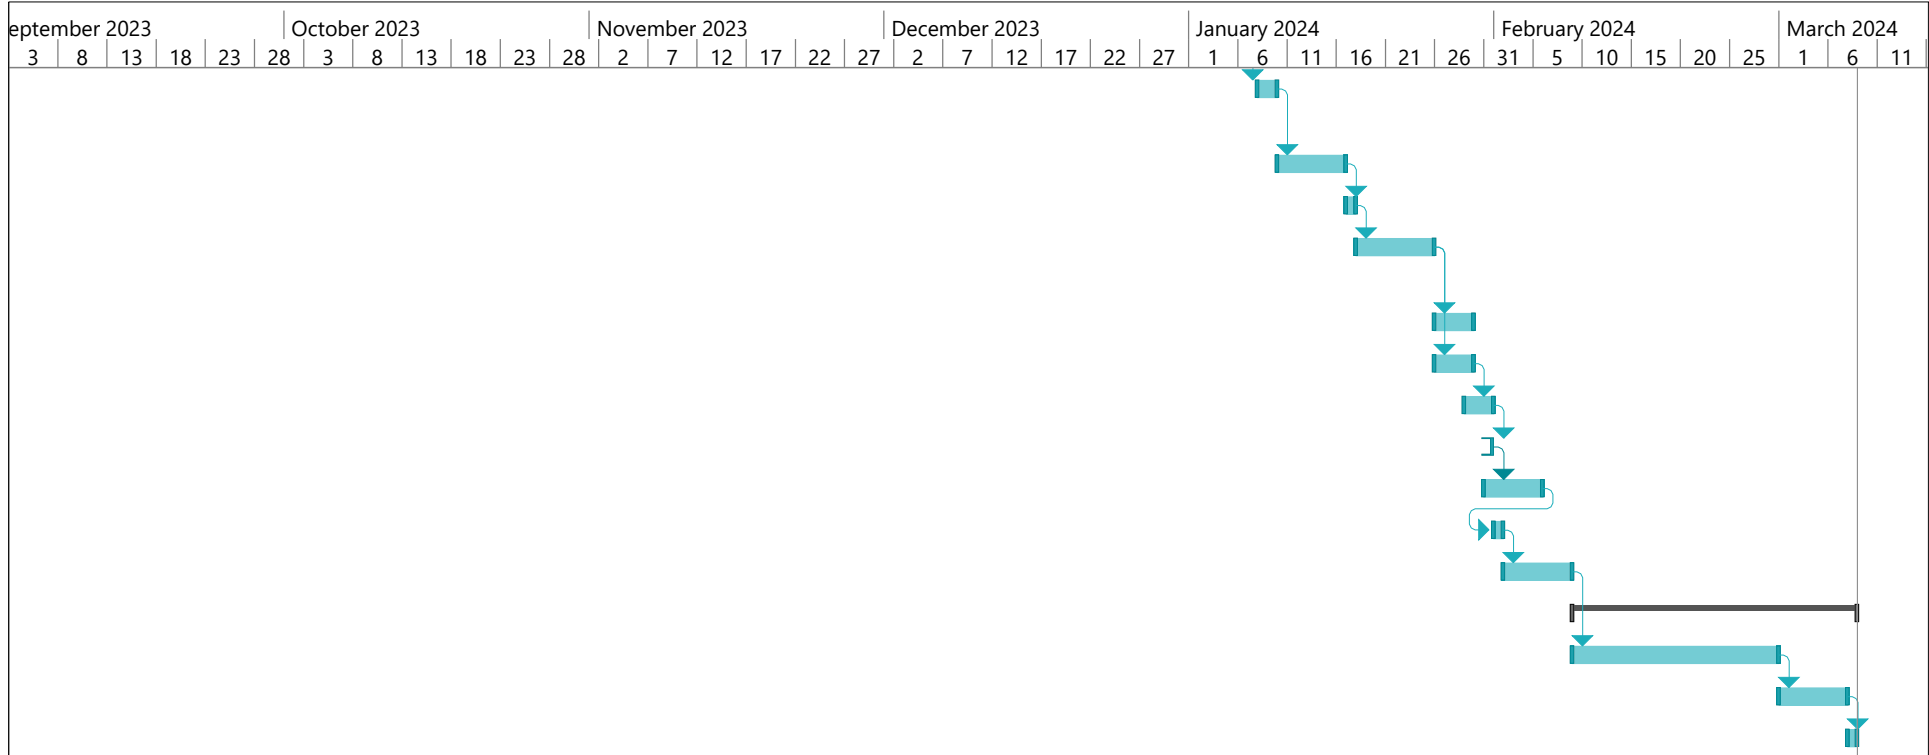

Project: 23rd Street Schedule 8. Date: Fri 8/18/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
