ID	Task Mode	Task Name	Duration	Start
1		Notice To Proceed	1 day	Mon 1/25/21
2		Mobilization	4 days	Tue 2/23/21
3		Site Traffic Control	10 days	Sat 2/27/21
4				
5		PHASE 1	60 days	Wed 6/2/21
6		Traffic Control Phase 1	2 days	Wed 6/2/21
7		Storm Sewer, West Side 35th	20 days	Thu 6/3/21
8		Storm Sewer Pipe & Structures	10 days	Sat 6/26/21
9		Remove Asphalt & Base	10 days	Thu 7/8/21
10		6" Lime	8 days	Tue 7/20/21
11		8" Crushed Concrete Base	8 days	Thu 7/29/21
12		2" Asphalt Surface	3 days	Sat 8/7/21
13				
14		PHASE 2	171 days	Fri 2/26/21
15		Traffic Control Phase 2	3 days	Fri 2/26/21
16		Water Line, East Side 35th, 8"	16 days	Tue 3/2/21
17		Water Line Services	16 days	Tue 3/2/21
18		Storm Sewer Pipe & Structure	4 days	Mon 3/15/21
19		Remove Asphalt & Base	10 days	Wed 8/11/21
20		6" Lime	8 days	Mon 8/23/21
21		8" Crushed Concrete Base	8 days	Wed 9/1/21
22		2" Asphalt Surface	3 days	Fri 9/10/21
23				
24		PHASE 3, Sanitary Sewer Bores CANCELLED	17 days	Tue 9/14/21
25		Traffic Control, Ally Between Broadway & Sealy	2 days	Tue 9/14/21
26		~~12" Sanitary Sewer Bore~~	~~6 days~~	~~Mon 1/25/21~~
27		~~Sanitary Services~~	~~6 days~~	~~Mon 1/25/21~~
28		Remove Asphalt & Base	5 days	Tue 9/14/21
29		6" Lime	5 days	Mon 9/20/21
30		4" Asphalt Base	4 days	Sat 9/25/21
31		2" Asphalt Surface	3 days	Thu 9/30/21
32				
33		PHASE 4	183 days	Mon 3/22/21
34		Traffic Control, Sealy Ave.	2 days	Mon 3/22/21
35		8" Water Line, OPEN CUT	6 days	Tue 3/23/21
36		Water Line Services	6 days	Tue 3/23/21

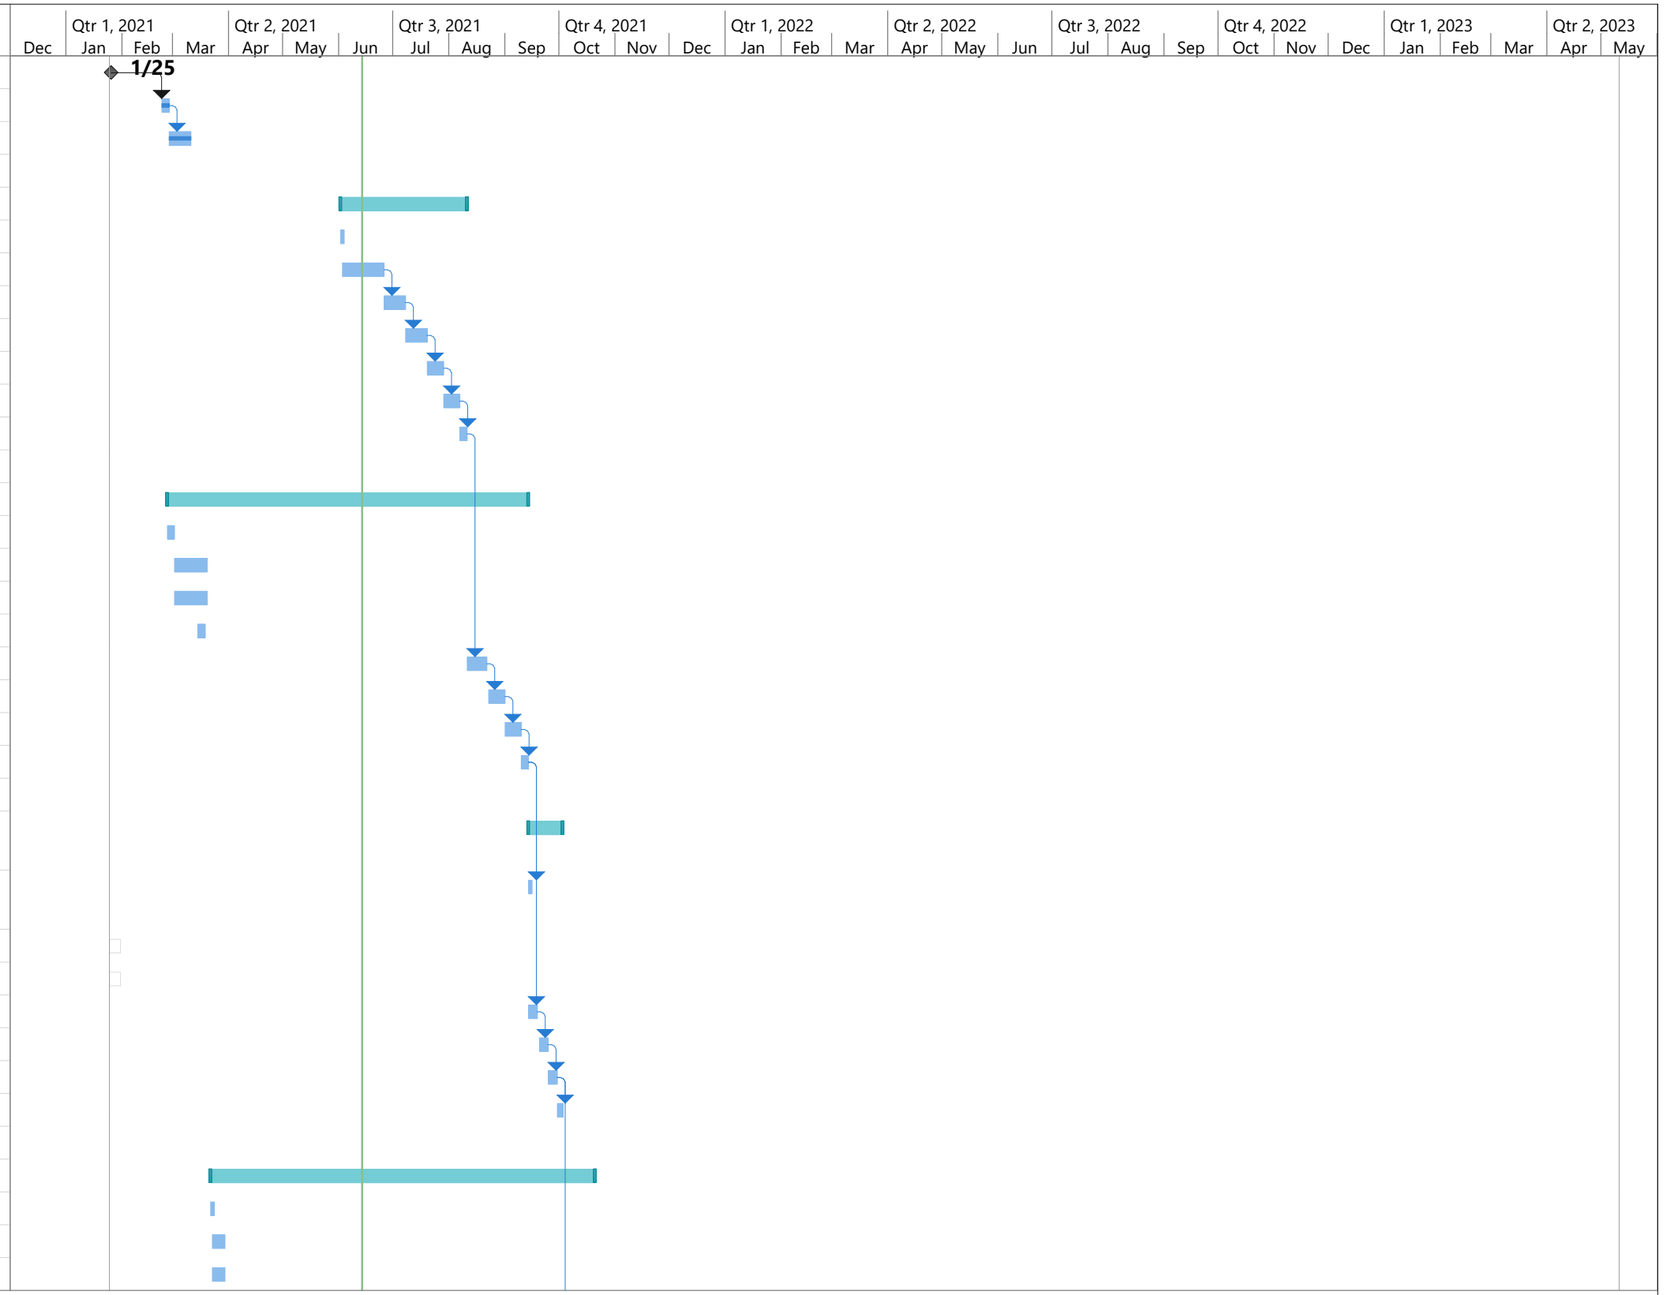

Project: 35th Street Roadway
Date: Mon 6/14/21

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

ID	Task Mode	Task Name	Duration	Start
37		Remove Asphalt & Base	5 days	Thu 9/30/21
38		6" Lime	5 days	Wed 10/6/21
39		8" Crushed Concrete Base	5 days	Tue 10/12/21
40		2" Asphalt Surface	3 days	Mon 10/18/21
41				
42		PHASE 5	149 days	Fri 5/21/21
43		Traffic Control, Alley Between Sealy & Ball	2 days	Fri 5/21/21
44		10" Sanitary Line Bore	5 days	Mon 5/24/21
45		Sanitary Services	5 days	Mon 5/24/21
46		Remove Asphalt & Base	5 days	Thu 10/21/21
47		6" Lime	5 days	Wed 10/27/21
48		4" Asphalt Stabilized Base	5 days	Tue 11/2/21
49		2" Asphalt Surface	3 days	Mon 11/8/21
50				
51		PHASE 6	212 days	Tue 3/30/21
52		Traffic Control, Ball Ave.	2 days	Tue 3/30/21
53		8" Water Line, OPEN CUT	7 days	Thu 4/1/21
54		Water Line Services	7 days	Thu 4/1/21
55		Remove Asphalt & Base	5 days	Thu 11/11/21
56		6" Lime	5 days	Wed 11/17/21
57		8" Crushed Concrete Base	5 days	Tue 11/23/21
58		2" Asphalt Surface	3 days	Mon 11/29/21
59				
60		PHASE 7	174 days	Thu 6/3/21
61		Traffic Control, Between Ball Ave. & Winnie Ave.	2 days	Thu 6/3/21
62		10" Sanitary Sewer Bore	2 days	Thu 6/3/21
63		Sanitary Services	2 days	Thu 6/3/21
64		8" Sanitary Sewer Bore	5 days	Sat 6/5/21
65		Sanitary Services	5 days	Fri 6/11/21
66		Remove Asphalt & Base	5 days	Thu 12/2/21
67		6" Lime	5 days	Wed 12/8/21
68		4" Asphalt Stabalized Base	5 days	Tue 12/14/21
69		2" Asphalt Surface	3 days	Mon 12/20/21
70				
71		PHASE 8	241 days	Fri 4/9/21
72		Traffic Control, Winnie Ave.	2 days	Fri 4/9/21

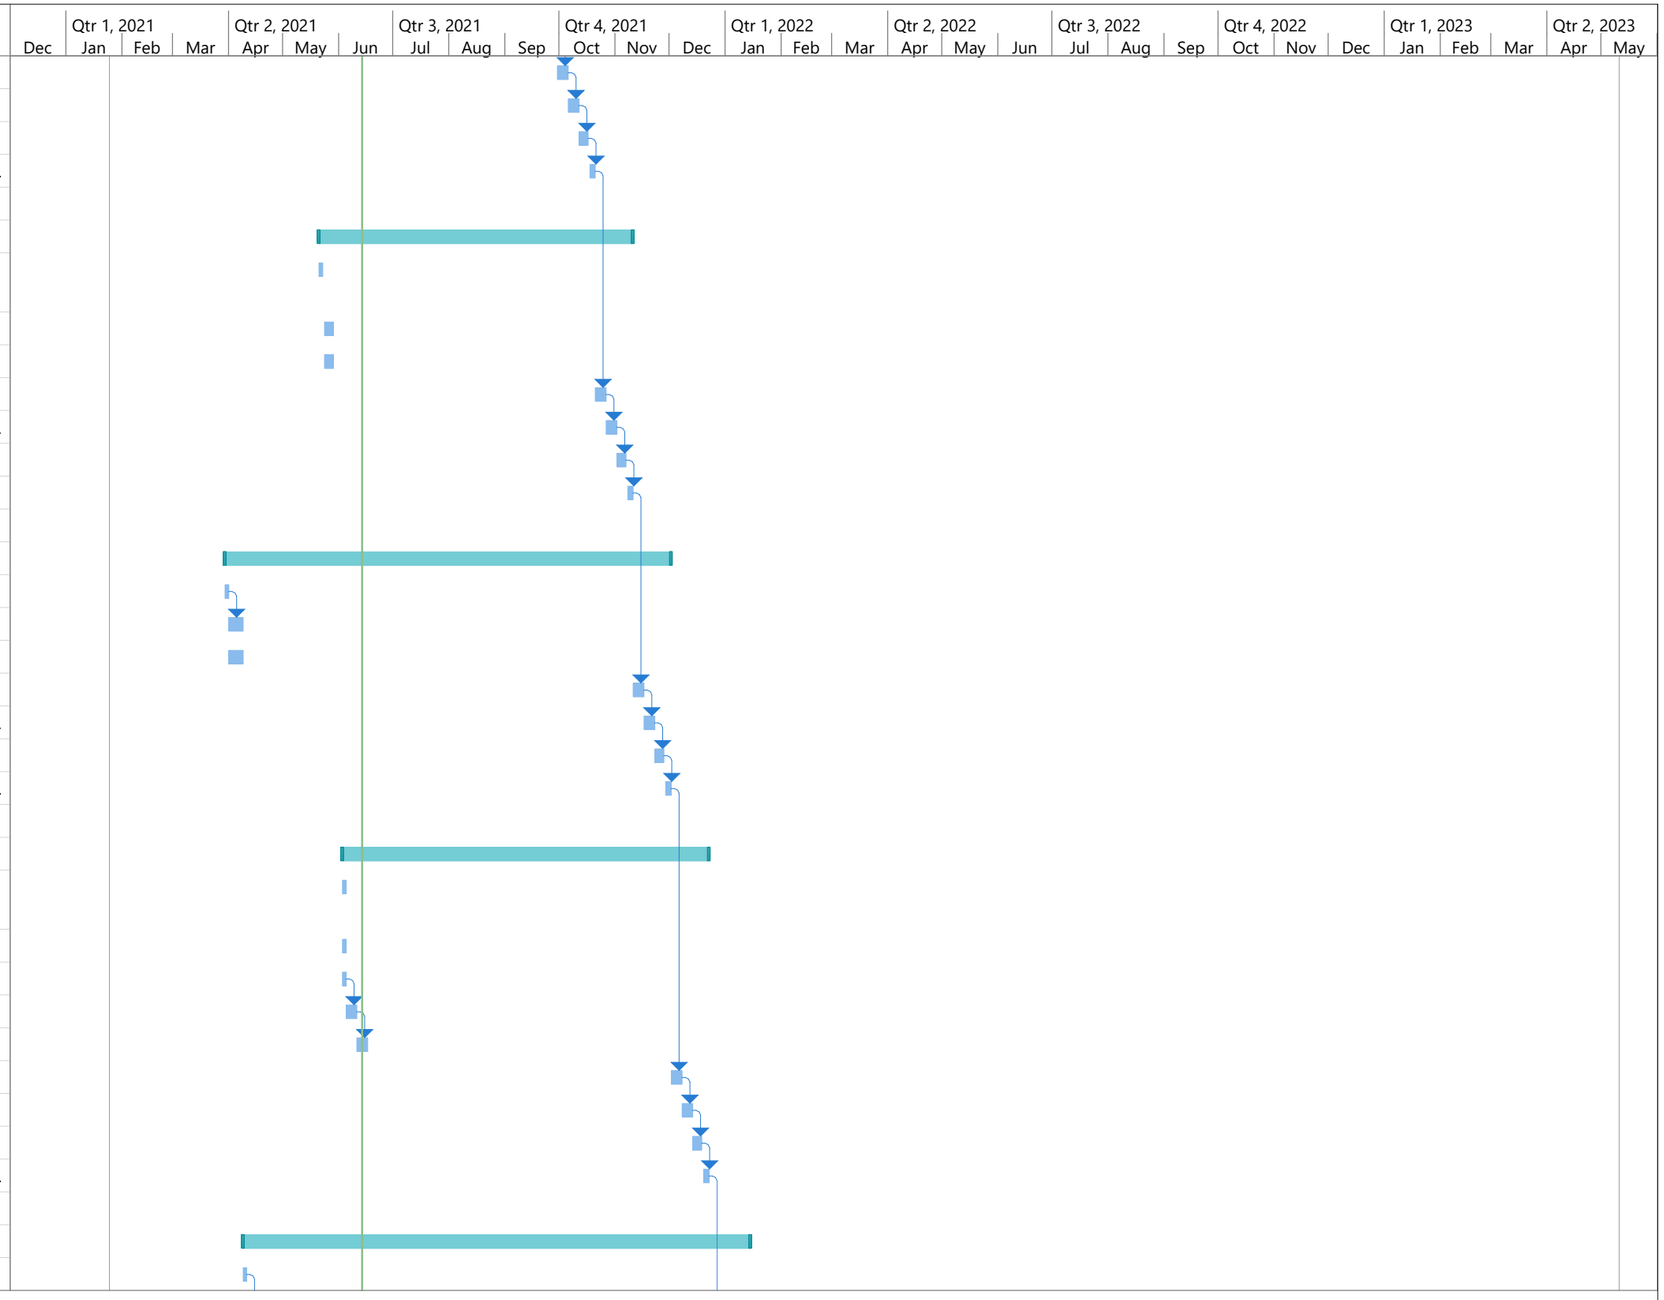

Project: 35th Street Roadway
Date: Mon 6/14/21

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

ID	Task Mode	Task Name	Duration	Start
73		8" Water Line, OPEN CUT	17 days	Mon 4/12/21
74		Water Line Services	17 days	Mon 4/12/21
75		Remove Asphalt & Base	7 days	Thu 12/23/21
76		6" Lime	5 days	Fri 12/31/21
77		8" Crushed Concrete Base	5 days	Thu 1/6/22
78		2" Asphalt Surface	3 days	Wed 1/12/22
79				
80		PHASE 9	219 days	Fri 5/28/21
81		Traffic Control, Between Winnie & Church Steet	2 days	Fri 5/28/21
82		10" Sanitary Bore	2 days	Tue 6/1/21
83		Sanitary Services	2 days	Tue 6/1/21
84		Remove Asphalt & Base	5 days	Sat 1/15/22
85		6" Lime	5 days	Fri 1/21/22
86		4" Asphalt Base	5 days	Thu 1/27/22
87		2" Asphalt Surface	5 days	Wed 2/2/22
88				
89		PHASE 10	256 days	Thu 6/10/21
90		Traffic Control, Church Street	2 days	Tue 2/8/22
91		Remove Asphalt	8 days	Thu 2/10/22
92		2" Asphalt Surface	3 days	Sat 2/19/22
93		Sign & Stripe	20 days	Wed 2/23/22
94		Seeding & Clean-Up	15 days	Fri 3/18/22
95				
96		Substantial Completion Date	30 days	Tue 4/5/22
97		Final Completion Date	1 day	Tue 5/10/22
98				
99		1 Year Warranty Walk Through	1 day	Wed 5/10/23

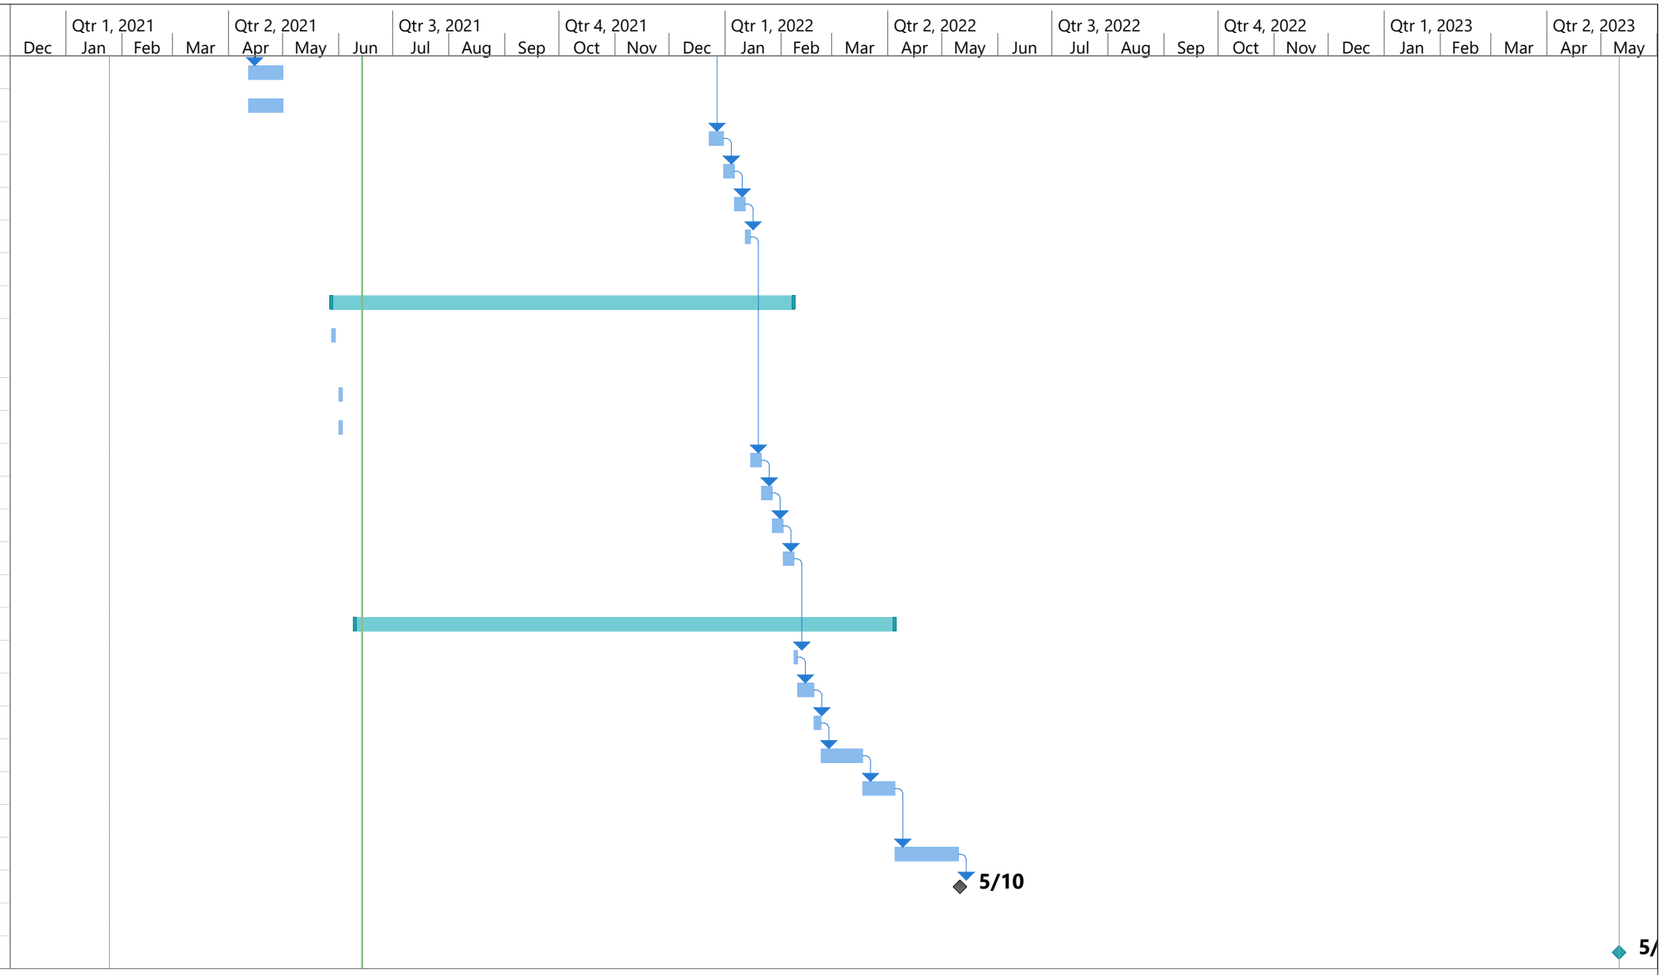

Project: 35th Street Roadway
Date: Mon 6/14/21

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
